



# xm1901: Orbital A

→ Week 8 – Tactical Kickoff
Week 6 - J-Asteroid 1
Week 5 - J-Asteroid 2
Week 4 - TCR approval and Handshake
Week 3 - Flight Activity Kickoff
Week 2 - Final Implementation/Delivery
Week 1 - Review/Uplink
Week 0 - Execution

- Week 2019-01
- Week: 12/31/2018 (DOY 365) T13:30:00 – 1/7/2019 (DOY 007) T13:30:00
- SPT: N/A
- Ops Engineer: Ed Audi
- OPSCHK: 130
- Science Activities: N/A
- Default attitude: Sun point through 1/1, Nadir Point after that
- Slew config: Default




# xm1901 Planning Schedule

Week 8 – Tactical Kickoff
Week 6 - J-Asteroid 1
Week 5 - J-Asteroid 2
Week 4 - TCR approval and Handshake
Week 3 - Flight Activity Kickoff
Week 2 - Final Implementation/Delivery
Week 1 - Review/Uplink
Week 0 - Execution

Activity	Start Date	Finish Date	Status
Tactical Kickoff	11/6/18	11/6/18	
OpNav Request	11/12/18	11/12/18	
New SOCR and kernel submission deadline	11/20/18	11/20/18	
OpsEng builds J-Asteroid Plan	11/21/18	11/28/18	
Deliver OpNav Checklist to FDS	11/29/18	11/29/18	
J-Asteroid Reconciliation	11/29/18	11/29/18	
Week TCR for BG sequence and science populated	12/3/18	12/3/18	
TCR approval	12/5/18	12/5/18	
Delivery to MSA	12/19/19	12/19/18	



# Data Product Completion Forecast

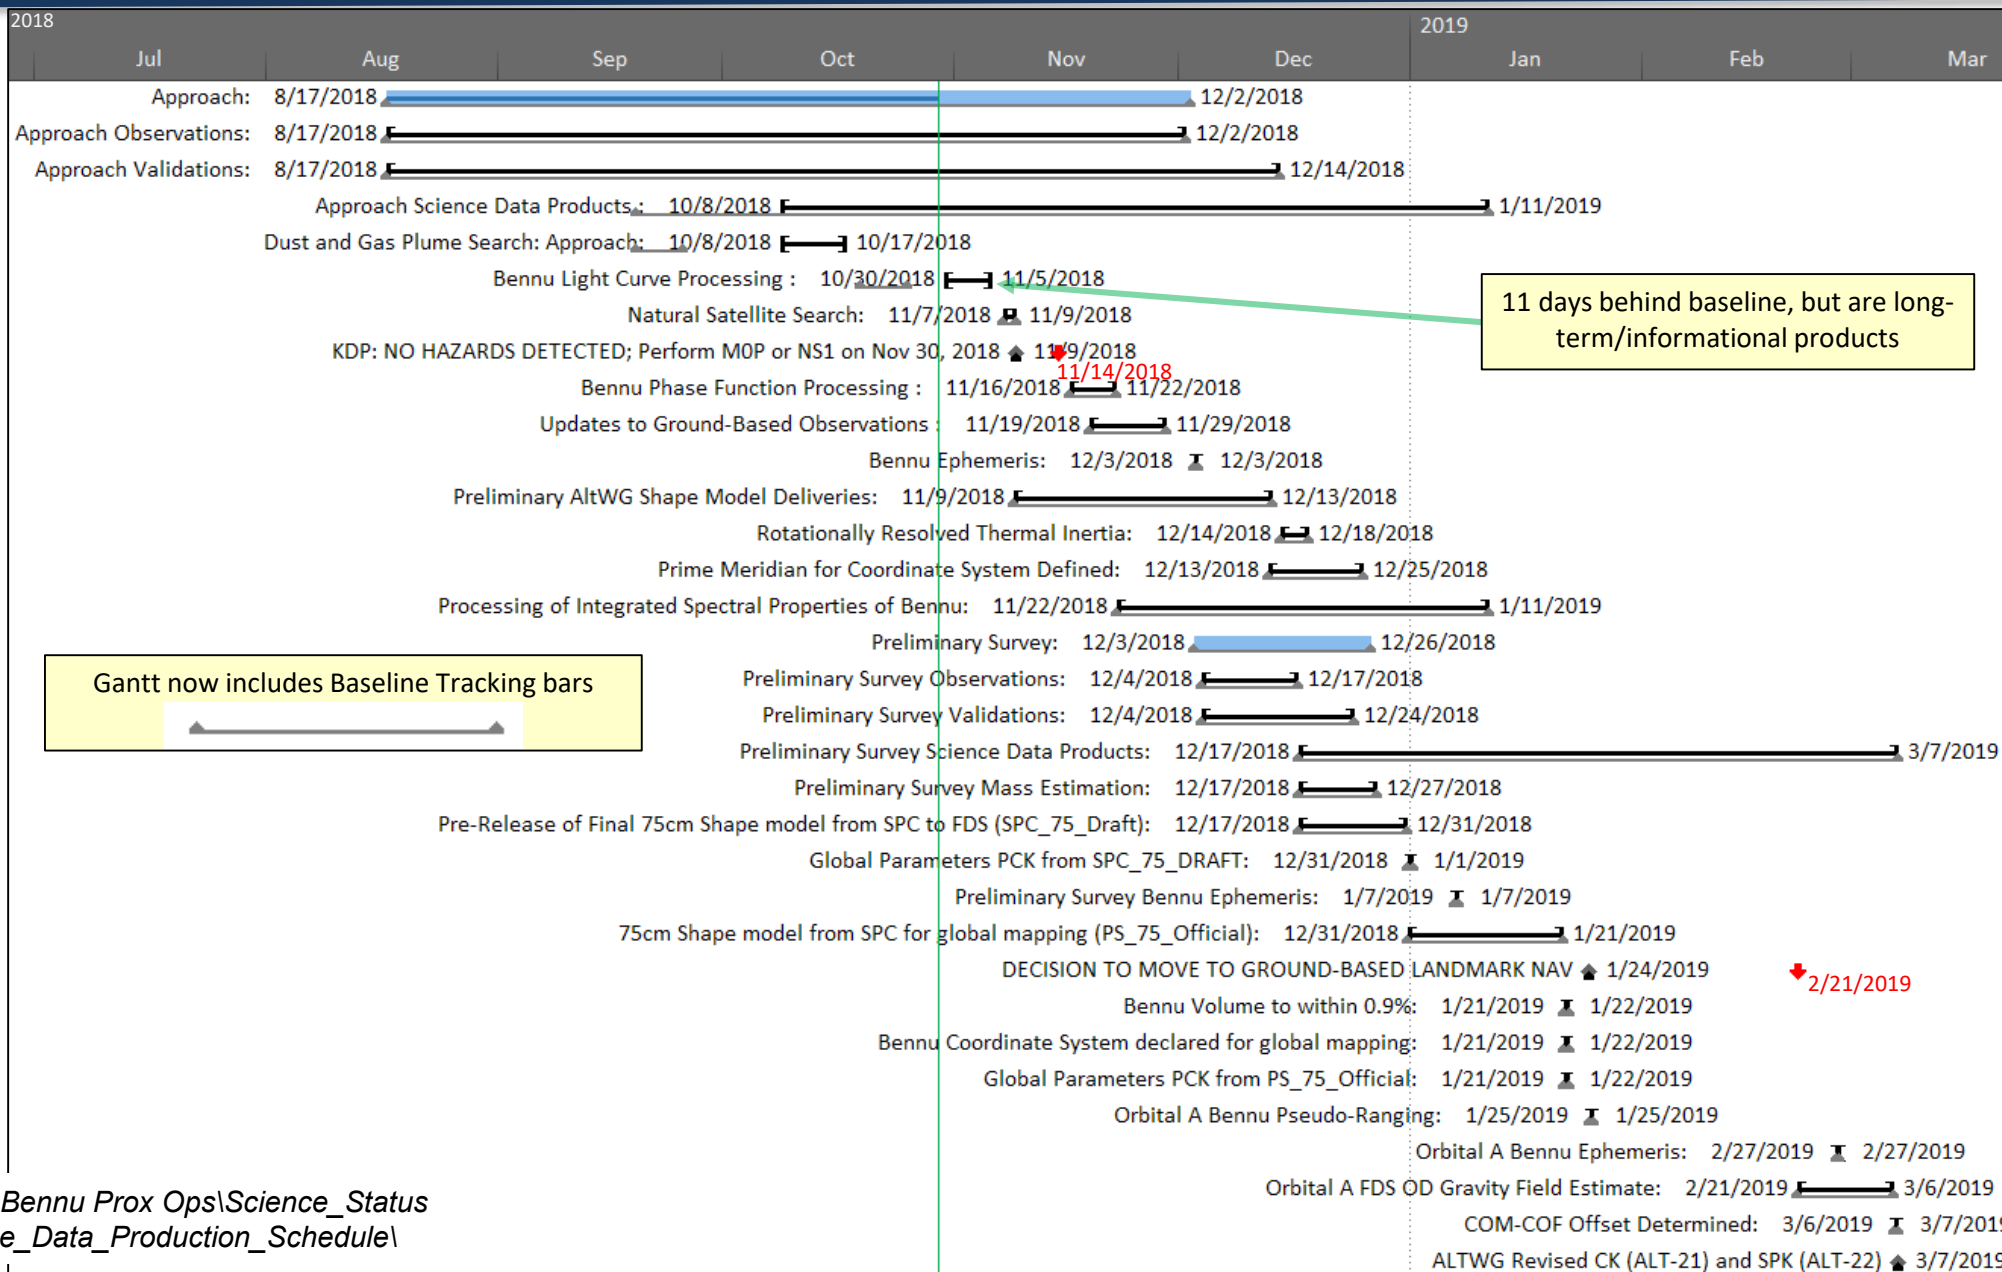

11 days behind baseline, but are long-term/informational products

Gantt now includes Baseline Tracking bars

